


One fifth of the 2025-2034 mining portfolio has yet to enter SEIA


US\$21,894m across 8 projects (20.9% of total investment)

Time to approval	Large EIAs approved by 24 months	Under review today	Approved investment
DIA 7.7 months (7.2-8.1) EIA 28.8 months (23.7-32.9)	26.4-49.8% bootstrap CI central estimate 38.4%	US\$24,780m 15 projects	US\$32,621m 31.2% of portfolio

Capital still without a filing accounts for one fifth

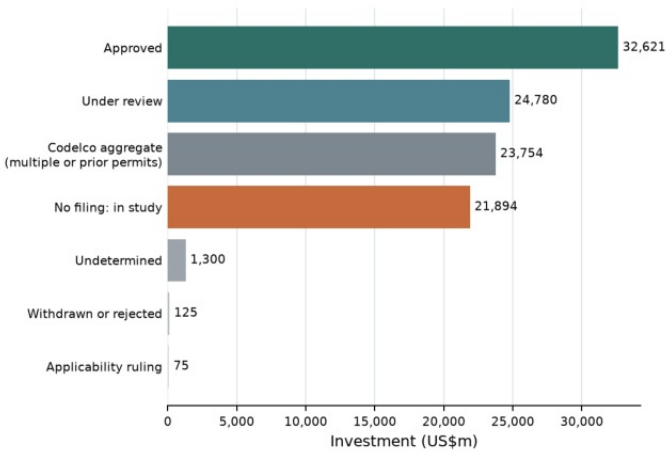

Competing risks lower observed approval

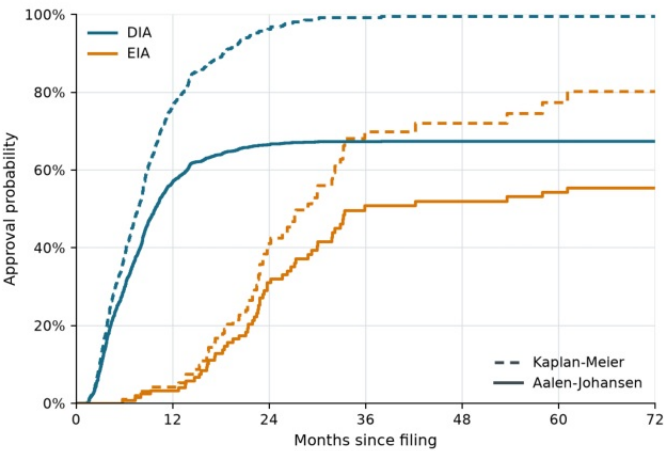

KM - Aalen-Johansen gap at 24 months: DIA +29.7 pp | EIA +10.1 pp

Implications for contractors

- The ~US\$21,900m tendering window depends on a permit not yet requested. At the EIA median, an RCA arrives at least ~2.4 years after filing.
- For large EIAs, only 1 in 4 to 1 in 2 are approved by 24 months: plan to that range, not Cochilco's commissioning dates.
- Litigation adds schedule risk: some rejections are later approved on appeal, and some RCAs are annulled by an environmental court.

Method and scope

Sources: Cochilco, Annex C (Dec-2025), and SEA (cut-off 2026-09-30).
Population: 1,645 admitted mining filings. Kaplan-Meier and Aalen-Johansen.
Unit: principal filing; modifications do not count as a match.
The 59-project match was manually validated; every figure has an independent recalculation.
A naive classification suggested 64% without a permit; after correcting projects in execution, operating subsidiaries, and aggregate rows, the figure is 21%.
