
16.5% of 2025–2034 mining investment is in study-stage projects with no identified SEIA filing


US$17,243m across 8 projects, all at study stage · SEA data to 25-08-2026

EIAs obtaining a favourable RCA	EIAs ≥US$100m with a favourable RCA at 24 months	Under review at SEA cut-off	Favourable RCA
31.7% at 24 months · n=124 51.7% at 36 months 50% at ~33 months	**39.6% (95% CI 27.6–52.0) · n=81**	**US$24,580m · 14 projects**	**US$37,597m · 36.0% of portfolio**

2025–2034 portfolio by SEIA status (US$m)

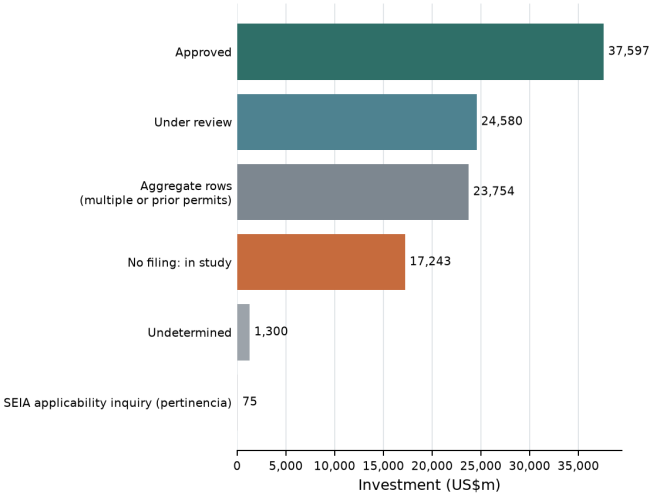

Ignoring withdrawals, rejections and early terminations (Kaplan–Meier) overstates favourable-RCA incidence

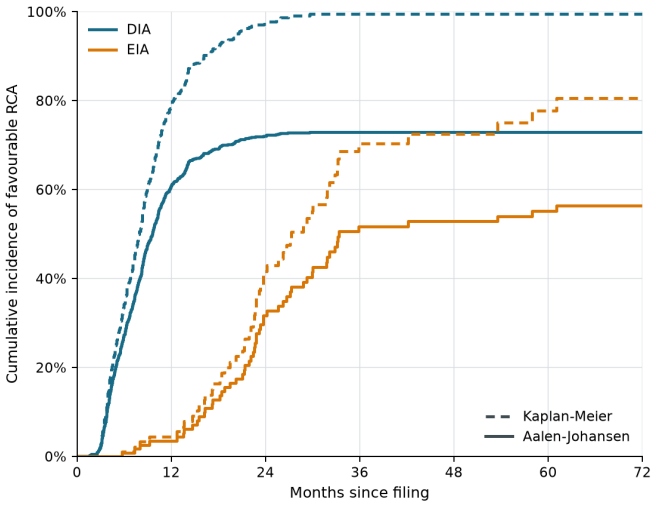

Implications for contractors

- As of the cut-off, these ~US$17,200m have no SEIA filing on record. As a descriptive historical reference, 31.7% of mining EIAs obtained a favourable RCA within 24 months; this is not a probability for those projects.
- As a descriptive historical reference, 39.6% of EIAs ≥US$100m obtained a favourable RCA within 24 months (95% CI 27.6–52.0%); it does not predict the Cochilco portfolio's outcomes.
- Separately, 4 aggregate rows in execution (US$23,754m) bundle several projects with multiple or prior permits; they are not assigned a unique filing and are excluded from the headline.

Method and scope

Sources: Cochilco, 2025–2034 Mining Investment Project Portfolio (Annex C, Dec-2025). SEA: downloaded 30-09-2026; latest record 25-08-2026.

Population: 995 admitted mining filings entered between 2011 and 2026; excludes sand-and-gravel (áridos) filings. Kaplan–Meier and Aalen–Johansen; months = days/30.44.

Portfolio: one principal filing per project; modifications do not count as a match. Times: each filing, including re-entries.

All 59 projects were reviewed one by one against SEA. Headline sensitivity: 8.8% excluding the largest judgment-call project; 40.5% adding aggregate rows and the undetermined case.

Favourable RCA includes 1 project (US$4,851m) whose valid RCA has an update under review.

Every published figure passes a programmatic control; the register labels each recalculation as independent, arithmetic control, or replica.
