


20.9% of 2025–2034 mining investment has no identified SEIA filing


US\$21,894m across 8 projects, all at study stage · SEA data to 25-08-2026

Cumulative EIA approval	EIAs ≥US\$100m approved at 24 months	Under review at SEA cut-off	Favourable RCA
31.7% at 24 months · 51.7% at 36 months · 50% at ~33 months	39.6% (95% CI 27.6–52.0) · n=81	US\$24,780m · 15 projects	US\$32,746m · 31.3% of portfolio

Study-stage projects with no identified filing: 20.9% of investment

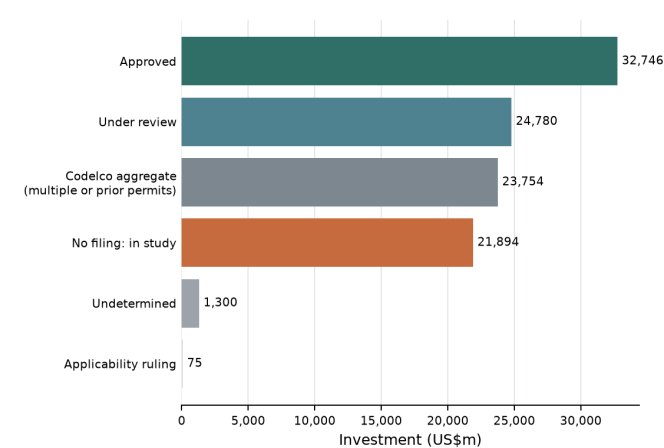

Ignoring withdrawals and rejections (Kaplan–Meier) overstates approval

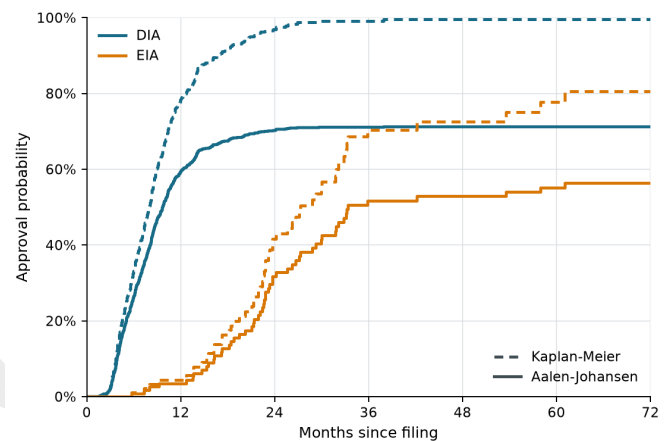

Implications for contractors

- These ~US\$21,900m still need to enter SEIA before construction. At 24 months after filing, 31.7% of EIAs are approved.
- For EIAs ≥US\$100m, we estimate 39.6% approved at 24 months (95% CI 27.6–52.0%): permit schedules should include contingency beyond Cochilco's commissioning dates.
- The figure may be higher: 4 aggregate Codelco rows (US\$23,754m) cannot be assigned a unique filing.

Method and scope

Sources: Cochilco, 2025–2034 Mining Investment Project Portfolio (Annex C, Dec-2025). SEA: downloaded 30-09-2026; latest record 25-08-2026. Population: 1,126 admitted mining filings entered between 2011 and 2026; excludes aggregates. Kaplan–Meier and Aalen–Johansen; months = days/30.44. Portfolio: one principal filing per project; modifications do not count as a match. Times: each filing, including re-entries. 38 of 59 matches reviewed filing by filing. Headline sensitivity: 8.6%–44.9% under 2 classifications and aggregate rows. Figures recalculated by an independent script; code and data in the repository.
